
BACK IN 1999

UNITED STATES POPULATION: 272.7 MILLION

AVERAGE INCOME: \$40,810.00



LENNY KRAVITZ SARA McLACHLAN BRITNEY SPEARS ENRIQUE IGLESIAS



FURBY BABIES
BEANY BABIES
GAME BOY COLOR
HAPPENIN' HAIR BARBIE
SEGA DREAMCAST



US PRESIDENT Bill Clinton



MOVIES

STAR WARS EPISODE I THE SIXTH SENSE TOY STORY 2 THE MATRIX



TV SHOWS

THE X-FILES
BEVERLY HILLS 90210
FRASIER
THE PRACTICE
7TH HEAVEN

WHAT THINGS COST:

 BREAD
 \$0.89
 • MOVIE TICKET
 \$5.08

 GALLON OF GAS
 \$1.17
 • GALLON OF MILK
 \$2.84

 POSTAGE STAMP
 \$0.33
 • NEW HOUSE
 \$195,600.00



- -WORLD POPULATION EXCEEDED 6 BILLION
- -Y2K AND MILLENIUM BUG CONCERNS
- THE INITIAL RELEASE OF NAPSTER
- -SWIFFER SWEPT THE NATION BY STORM
- -WEST NILE VIRUS FIRST APPEARS IN THE US

LIVELAUGHROWE.COM

YOU WAITED FOR AOL TO DIAL UP THE INTERNET

YOU WERE LISTENING TO MESSAGES ON AN ASWERING MACHINE

USED PHONE BOOKS AND YELLOW PAGES

BLOCKBUSTER WAS THE HOT SPOT FOR RENTING MOVIES

Worth the Wait

Lake Land College Luther Student Center

LAKE LAND COLLEGE

presented by

Madge Shoot Comptroller, Lake Land College

Ryan VenHuizen Senior Project Architect, Legat

Sylvia Kowalk Director of Interior Design, Legat

4/21/2022



LEGATARCHITECTS



Dr. Robert K Luther

Project Timeline

```
1999 _ Initial approval of the Capital Project
2002 Lake Land initiate project
2001 _ 1st Groundbreaking
2003 Project placed on hold by Illinois CDB
2006 _ 2<sup>nd</sup> Groundbreaking
2012 Lake Land initiates Architect approval process
2013 Design #1 Begins (CDB project)
2014 Funding for Design #1
2015 State Budget Impasse
2018 Design #2 Begins
2018 _ 3rd Groundbreaking
2018 Issue for Bid
2019 Construction Completed
```







AFTER 6 GOVERNORS













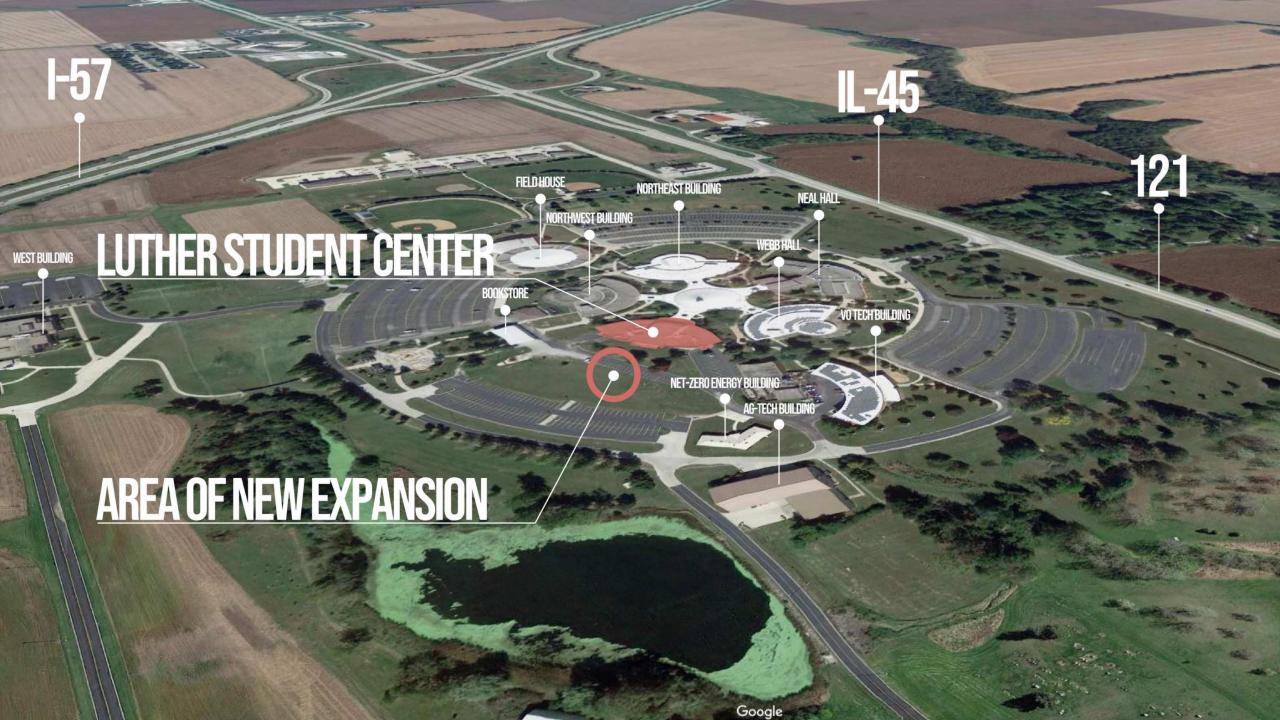

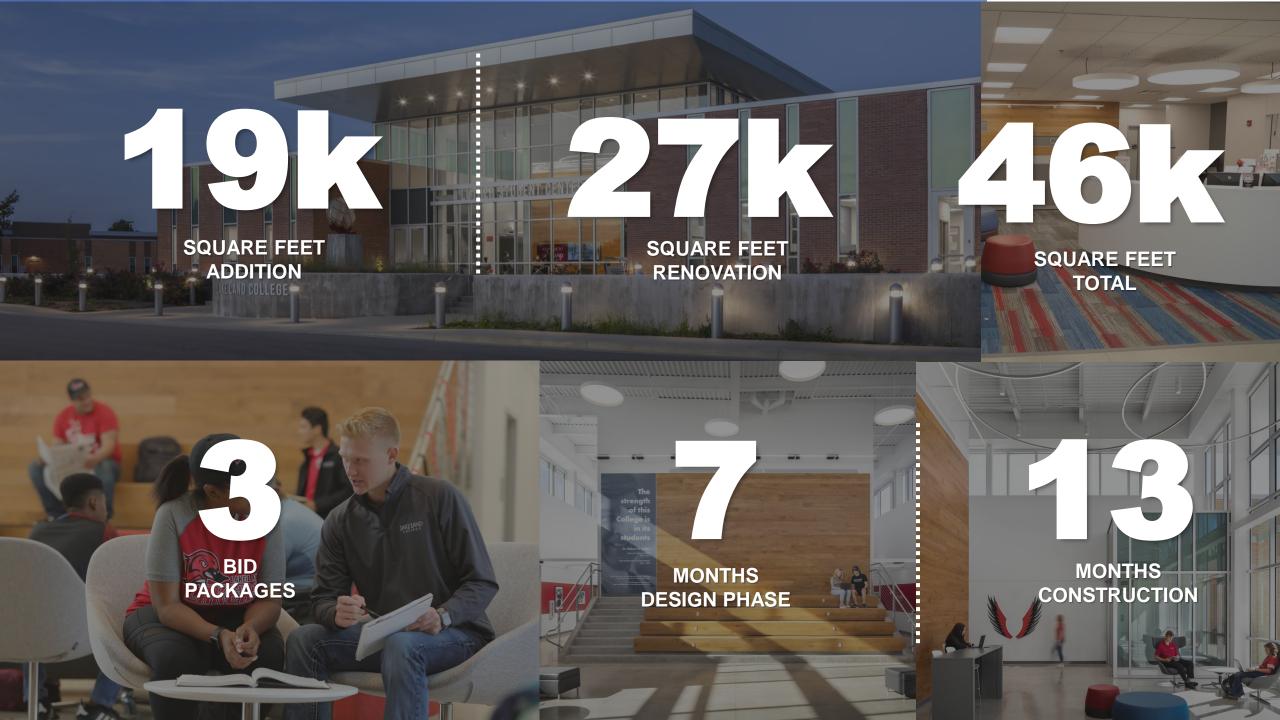


	CONSTRUCTION COST	PROJECT COST
BUDGET	\$10.0M	\$14.0M
BODGET	Ψ10.0141	γ1-1.0141
COST ESTIMATE	\$10.24M	\$14.23M
0001 20111111/1/12	ΨΙΟΙΖΙΙΨΙ	Ψ11.23141
COST PER SQ/FT	\$329 SQ/FT	\$444 SQ/FT
	φ323 3331 1	φ 11136()11
ACTUAL	\$10.13M	\$14.08M
7.0.07.1	723:23:11	·
DELTA		

Spirit Shop / Bookstore Computer Lab Student Life Campus Police Admissions Accounting Counseling Transfer Services Veteran Services Career Services Financial Aid Food Services Nurse TRIO







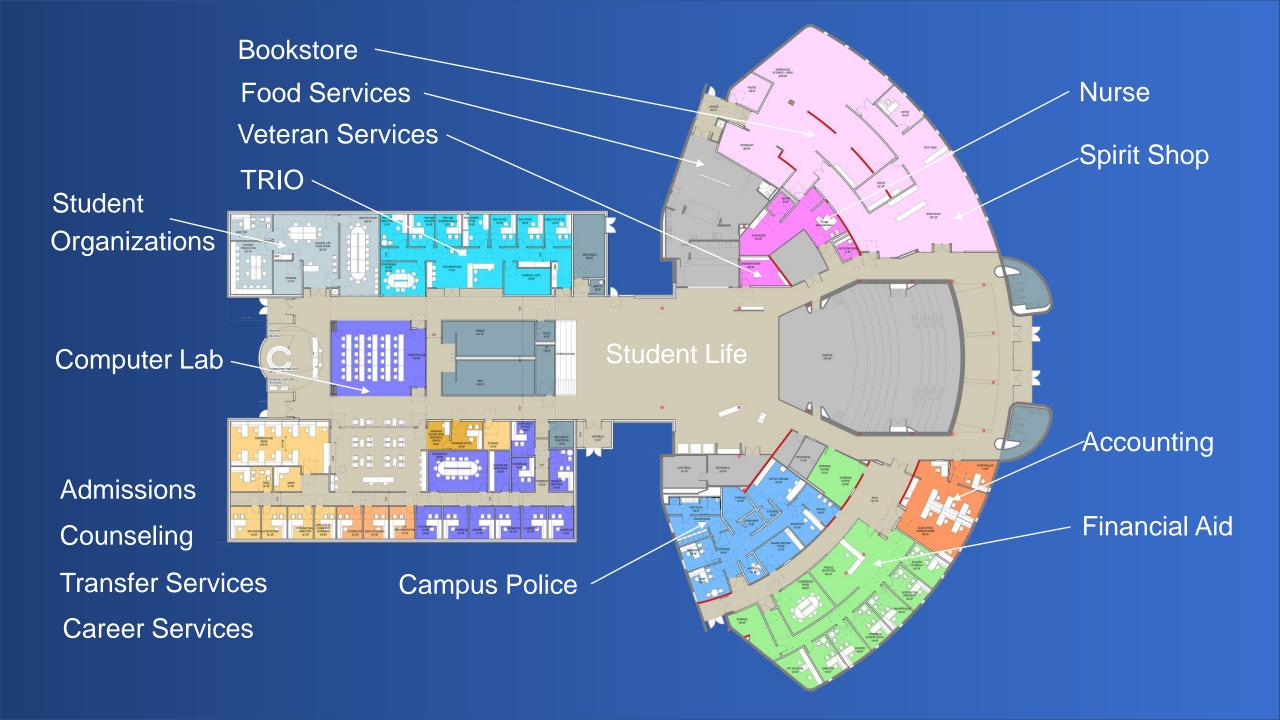

CHANGE ORDERS

UNFORSEEN CONDITIONS

\$6,552 (0.07%)

ARCHITECT / ENGINEER OMISSIONS


\$9,053 (0.09%)

OWNER REVISIONS / ADDITIONS

\$63,158 (0.62%)


TOTAL (% OF CONSTRUCTION COST)

0.76% (A+)

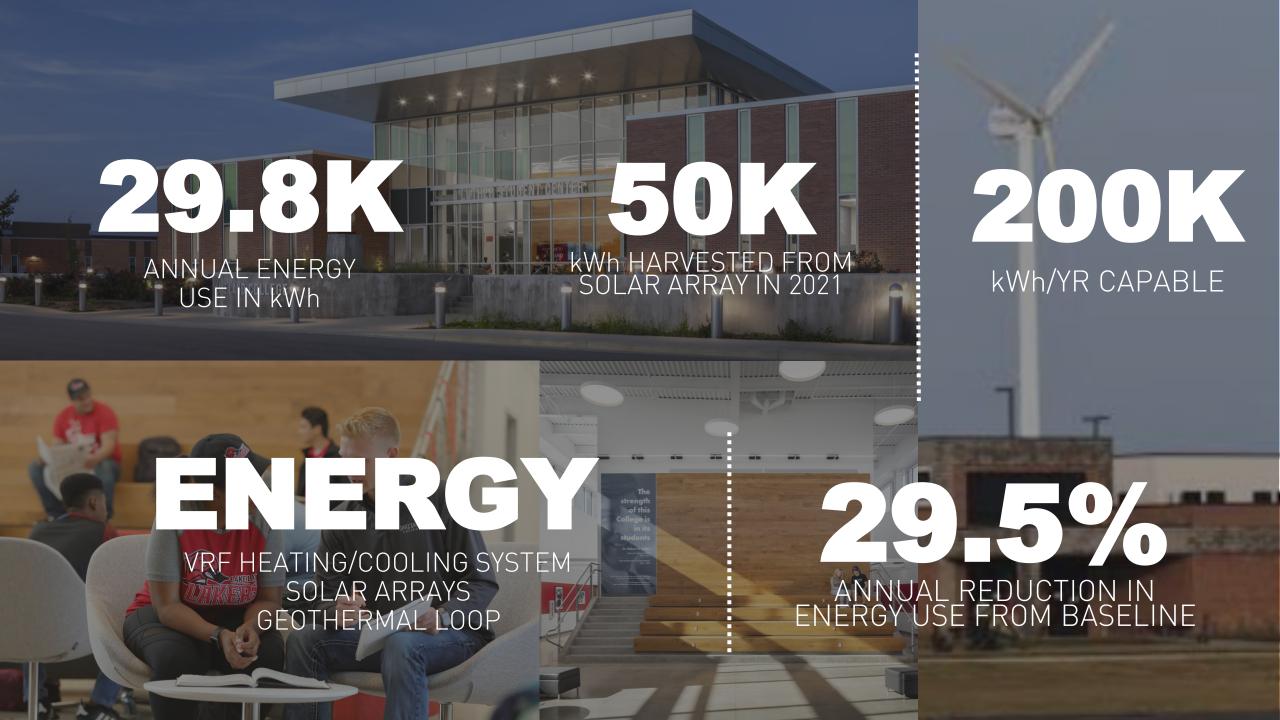




Mechanical Equipment Concealment Strategy

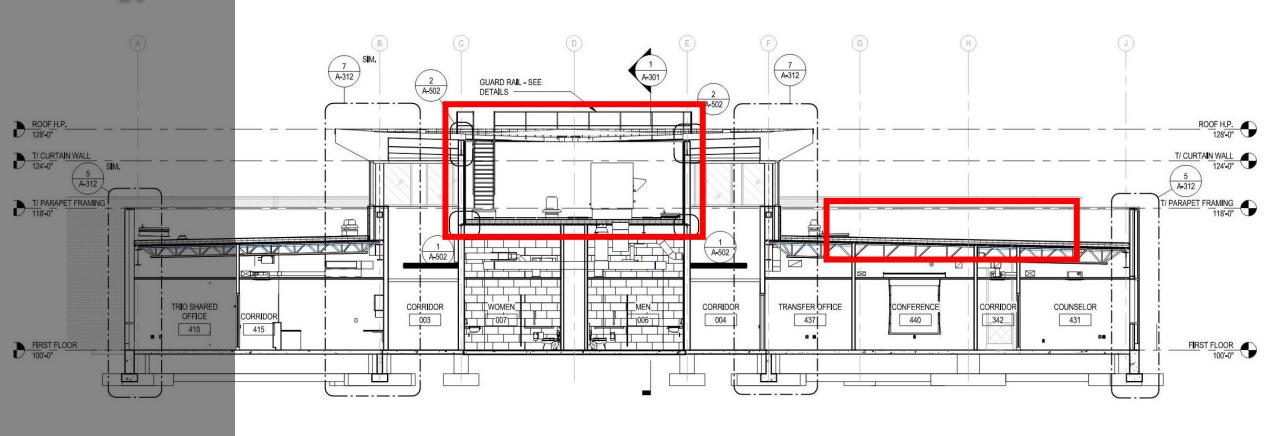


Pattern /
Movement /
Visual Energy /
Cost

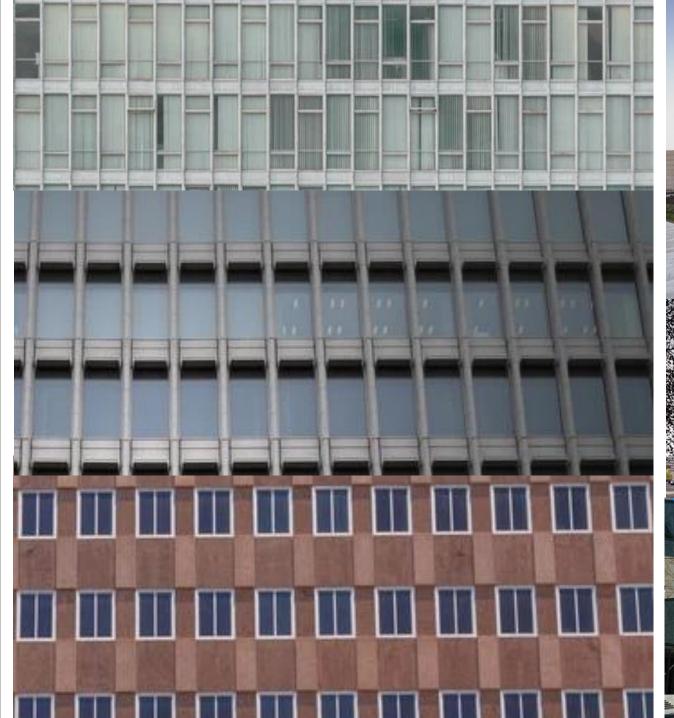





LONGITUDINAL WAVES



Rhythmic Patterning











Environmental Graphics I Signage



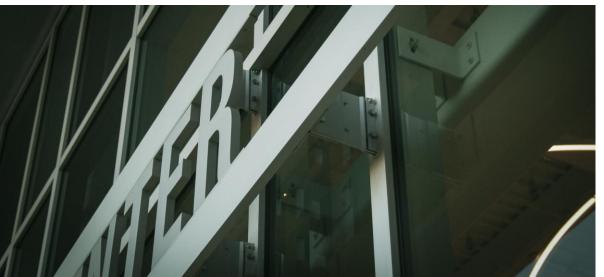

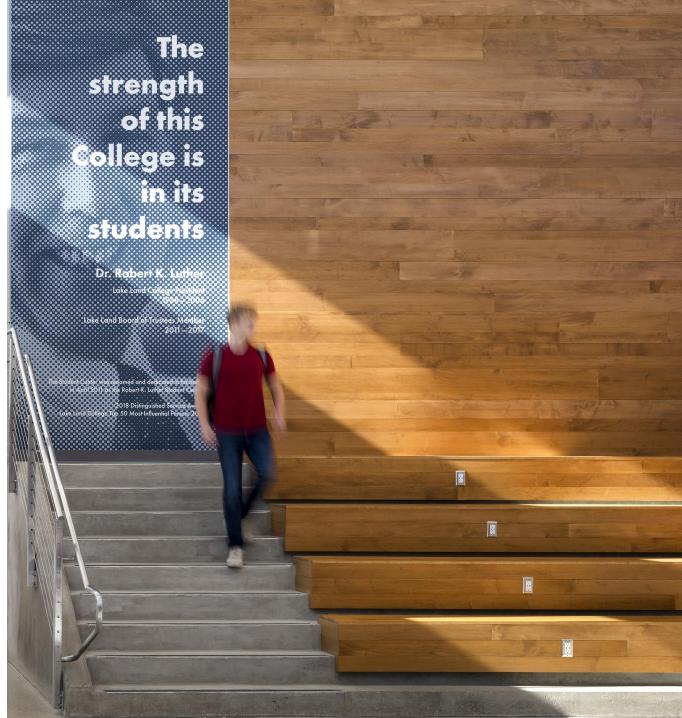








Before



After



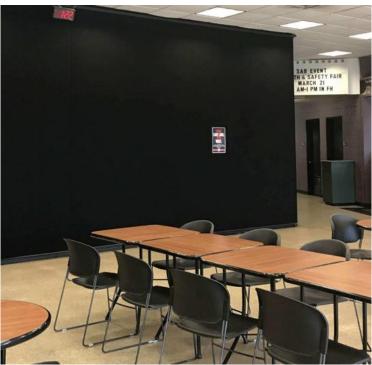




Before







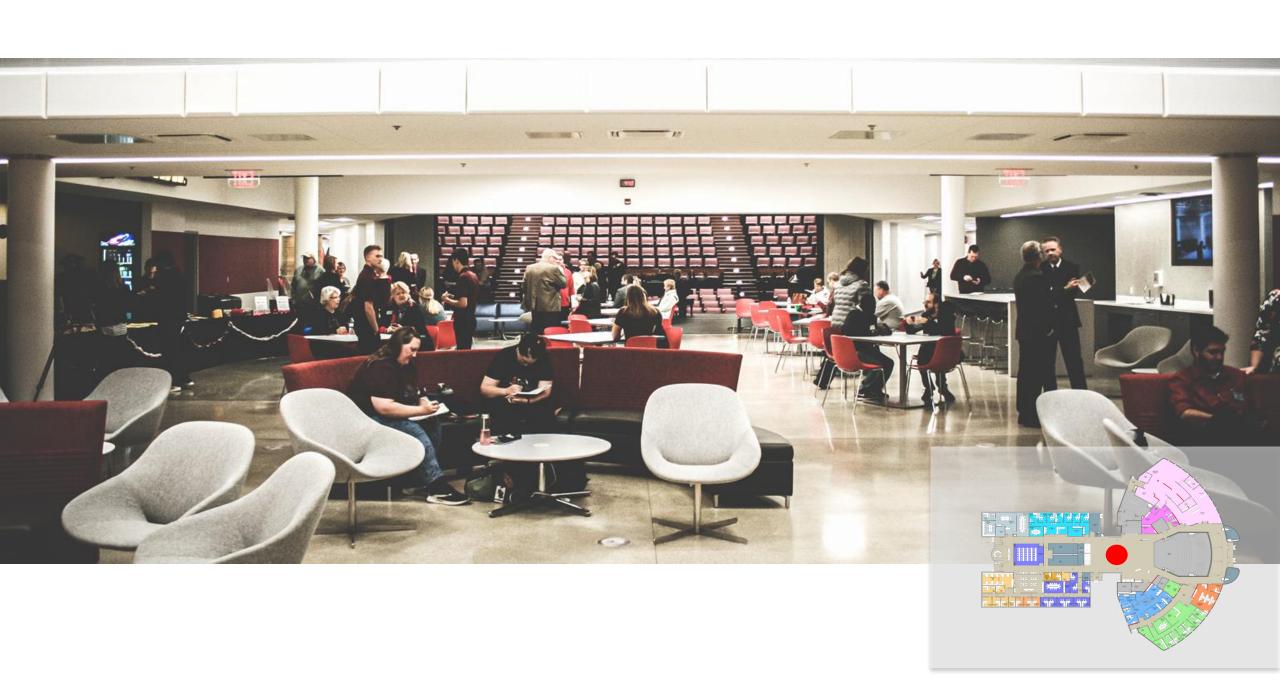
















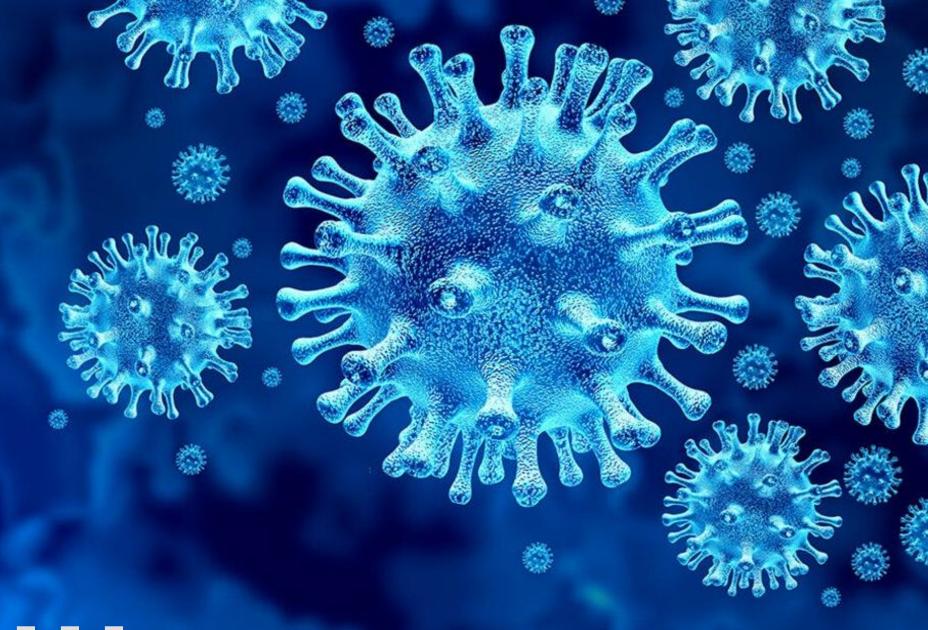

2019...



Worth the wait...

LEGATARCHITECTS

